


State Route 750/Powell Road Widening ODOT PROJECT UPDATE

An early Spring means crews have already resumed work on State Route 750, more commonly known as Powell Road. The \$6 million project that began last Fall will reduce congestion and improve safety by:

- Widening SR 750 to five lanes between Gibson Drive and Old Sawmill Road
- Building a 10 foot multi-use path on the north side of SR 750
- Constructing dual left turn lanes at Sawmill Parkway and SR 750 for northbound, southbound and eastbound traffic at the intersection

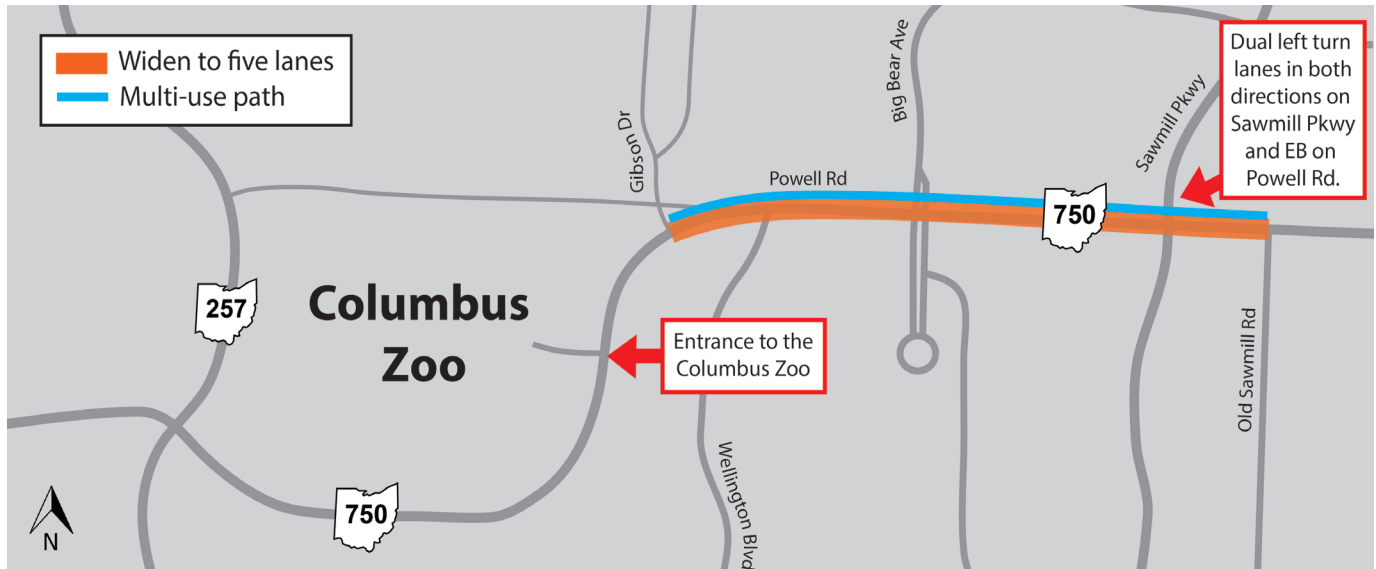

Project Schedule & Impacts to Traffic

Now until the end of May:

- SR 750 traffic has been shifted to the north so crews can widen the south side of SR 750.
- Sawmill Parkway is reduced to one southbound lane south of the SR 750 intersection so crews can widen the west side of Sawmill Parkway.
- Sawmill Parkway will be reduced to one northbound lane north of SR 750 for one week.
- The right-in, right-out driveways west and south of SR 750 and Sawmill will be closed one at a time.

June to Mid-August:

- SR 750 traffic will be shifted to the south so crews can construct the north side of SR 750.
- When constructing Galloway Drive, traffic will be detoured to Sawmill Parkway.
- Farmington Avenue will close at SR 750 for one week.

Mid-July to Mid-August:

- Crews will work on the east side of Sawmill Parkway, north and south of the SR 750 intersection.
- Sawmill Parkway will be reduced to one lane.

Mid-August until September:

- The project team will pave the surface course and install final pavement markings.

PLEASE NOTE: Prior notification will be given before traffic is impacted.

QUESTIONS: Email d06.pio@dot.ohio.gov or call 740-833-8268
